


ID	Task Name	Duration	Start	Finish	2022		June 2022		July 2022		August 2022		September 2022		Oct														
					11	16	21	26	31	5	10	15	20	25	30	5	10	15	20	25	30	4	9	14	19	24	29	3	8
1	CITY OF MARQUETTE SIMP 2022	95 days	Mon 5/23/22	Fri 9/30/22																									
2	MOBILIZATION FOR SEWER LATERALS/STORM SEWER EAST NICOLET BLVD AND CENTER ST	5 days	Mon 5/23/22	Fri 5/27/22																									
3	EAST NICOLET BLVD-NICOLET BLVD TO ALLOUEZ ROAD SEWER LATERALS 10 EA	5 days	Mon 5/23/22	Fri 5/27/22																									
4	NO WORK MONDAY MAY 30 FOR MEMORIAL DAY HOLIDAY	1 day	Mon 5/30/22	Mon 5/30/22																									
5	EAST NICOLET BLVD STORM SEWER	3 days	Mon 5/30/22	Wed 6/1/22																									
6	CENTER STREET-WILKINSON STREET TO PRESQUE ISLE AVE SEWER LATERALS 16 EA	9 days	Thu 6/2/22	Tue 6/14/22																									
7	CENTER ST REMOVE AND REPLACE CURB AT LATERALS AND REPAIR AREAS	10 days	Mon 6/13/22	Fri 6/24/22																									
8	EAST NICOLET AND CENTER ST HMA TRENCH PATCHING	10 days	Mon 6/13/22	Fri 6/24/22																									
9	CENTER ST TOPSOIL , SOD RESTORATION	11 days	Thu 6/16/22	Thu 6/30/22																									
10	NO WORK FRIDAY JULY 1 AND MONDAY JULY 4 FOR JULY 4 HOLIDAY	2 days	Fri 7/1/22	Mon 7/4/22																									
11	MOBILIZATION CURB REMOVALS (McCLELLAN AVE, SUGARLOAF AVE, BLUFF ST	10 days	Mon 6/27/22	Fri 7/8/22																									
12	CURB REPLACEMENTS (McCLELLAN AVE, SUGARLOAF AVE, BLUFF ST)	10 days	Mon 7/11/22	Fri 7/22/22																									
13	TOPSOIL, SOD RESTORATION TO CURB REPAIR AREAS	10 days	Thu 7/14/22	Wed 7/27/22																									
14	MILLING (LONGYEAR AVE,CENTER ST, McCLELLAN AVE, SUGARLOAF AVE, BLUFF ST)	8 days	Tue 9/6/22	Thu 9/15/22																									
15	NO WORK MONDAY SEPT 5 FOR LABOR DAY HOLIDAY	1 day	Mon 9/5/22	Mon 9/5/22																									
16	EAST NICOLET CRUSH AND SHAPE	5 days	Mon 9/12/22	Fri 9/16/22																									
17	HMA PAVING	9 days	Mon 9/19/22	Thu 9/29/22																									
18	PAVEMENT MARKINGS/STRIPING	5 days	Mon 9/26/22	Fri 9/30/22																									
19	OVERBAND CRACK FILLING	15 days	Mon 8/8/22	Fri 8/26/22																									
20	PUNCHLIST/PROJECT CLOSEOUT	5 days	Mon 9/26/22	Fri 9/30/22																									

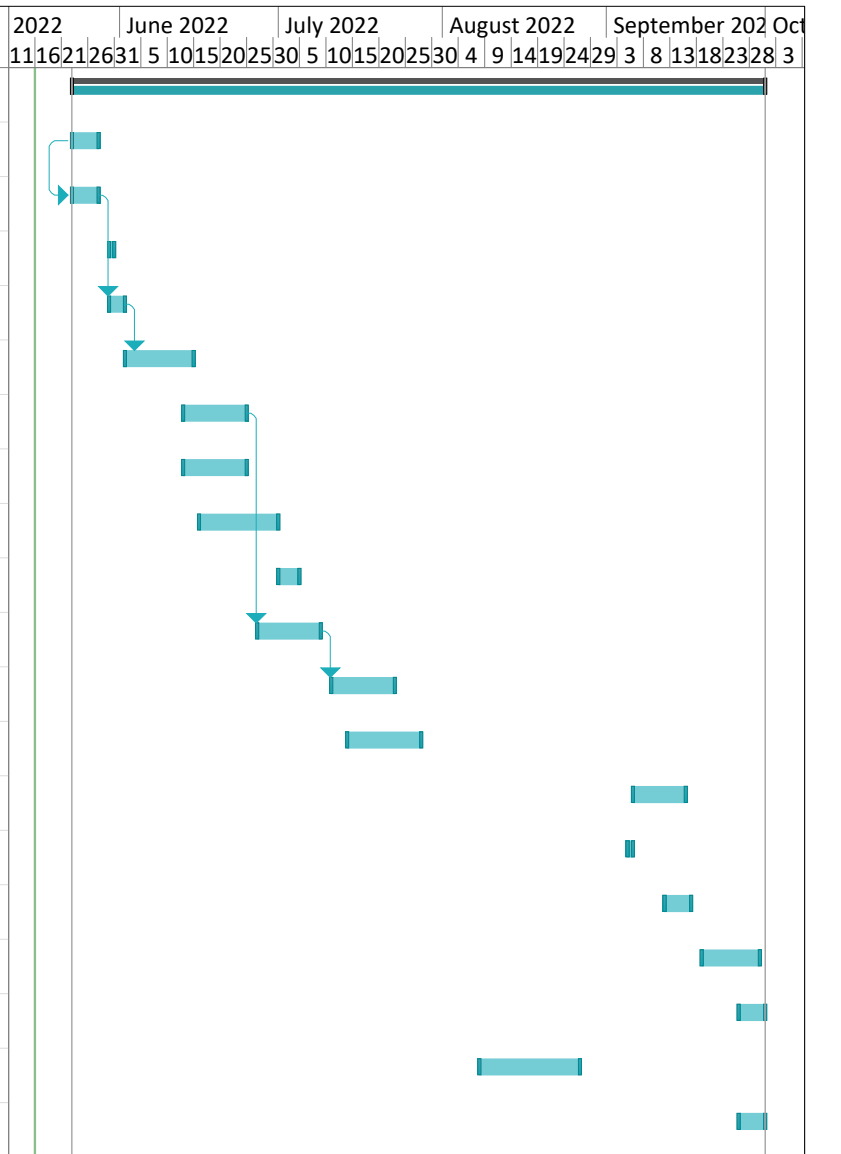

Project: Project Schedule Date: Mon 5/16/22	Task		External Tasks		Manual Task		Finish-only	
	Split		External Milestone		Duration-only		Deadline	
	Milestone		Inactive Task		Manual Summary Rollup		Progress	
	Summary		Inactive Milestone		Manual Summary		Manual Progress	
	Project Summary		Inactive Summary		Start-only			
